

EvCol — Event Collision Detector

UCS503 Software Engineering • Team Progress & Contribution Gantt Chart

Project Start	03-Aug-2026
Status Date	15-Sep-2026
Team Members	Jaskaran Singh
	Parmeet Singh
	Vaani Mehta


TASK / MILESTONE	OWNER	PROGRESS	START
Phase 1 — Inception & Requirements			
Problem definition, scope & user requirements	Jaskaran Singh	100%	03-Aug
Use-case analysis & system workflow	Vaani Mehta	100%	03-Aug
Level 1 DFD & system architecture	Parmeet	100%	05-Aug
Database schema & technology setup	All	100%	08-Aug
Phase 2 — Event Integration and Data Foundation			
External event API integration	Jaskaran Singh	100%	11-Aug
Event data normalization & validation	Parmeet Singh	100%	12-Aug
Elasticsearch event index setup	Vaani Mehta	100%	13-Aug
PostgreSQL user & session store	Jaskaran Singh	100%	19-Aug
Initial event dataset & ingestion pipeline	Vaani Mehta	100%	20-Aug
Phase 3 — Collision Scoring and Recommendations			
Temporal proximity & event relevance logic	Jaskaran Singh	100%	27-Aug
Audience overlap & event magnitude scoring	Vaani	100%	01-Sep
Explainable collision risk score	Parmeet	55%	05-Sep
Nearby-date search & alternative recommendations	Vaani	35%	08-Sep
Risk scoring API integration	All	20%	12-Sep
Phase 4 — Web Dashboard and User Features			
Dashboard development	Vaani	0%	15-Sep
Launch date submission interface	Jaskaran	0%	18-Sep

Risk score & conflicting-event display	Parmeet	0%	21-Sep
Alternative-date recommendation interface	Parmeet	0%	28-Sep
Phase 5 — Testing, Integration and CI/CD			
Frontend–backend–scoring integration	All	0%	05-Oct
API & database integration testing	Jaskaran	0%	05-Oct
Collision scoring validation & error analysis	Parmeet	0%	12-Oct
Performance & latency testing	Jaskaran	0%	19-Oct
GitHub Actions CI/CD pipeline	Vaani	0%	19-Oct
Phase 6 — Calendar Sync, Validation and Delivery			
Google/Outlook OAuth calendar synchronization	Jaskaran	0%	02-Nov
Historical launch-date validation	Vaani	0%	02-Nov
Usability & pilot testing	Parmeet	0%	09-Nov
Final documentation, demo & presentation	All	0%	16-Nov

LEGEND

Completed	In progress	Planned
-----------	-------------	---------

[illegible]

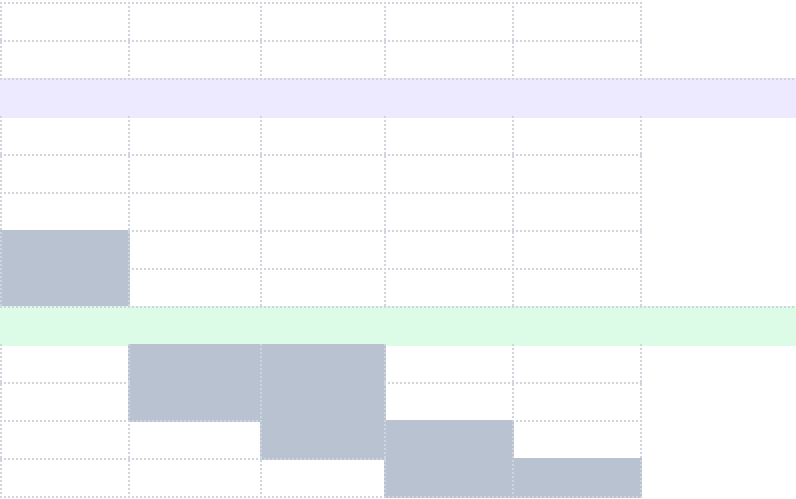

EvCol — TEAM CONTRIBUTION MATRIX

Planned ownership is balanced across product engineering, machine learning, and quality/deployment.

Member	Primary Responsibility	ML / Data	Frontend	Backend / DB
Jaskaran Singh	Event ingestion, backend/API & scoring logic	30%	40%	40%
Vaani Mehta	Data pipeline, Elasticsearch, recommendations & CI/CD	50%	30%	10%
Parmeet Singh	System architecture, database, dashboard & testing	20%	30%	40%

Shared / Joint Contributions

- Requirements, use cases, DFDs and system architecture
- Data pipeline integration and end-to-end prediction flow
- Integration testing, pilot validation and user feedback
- Final report, README, demonstration and presentation



DevOps / Testing	Documentation / PM	Planned Share
10%	Primary	33%
20%	Primary	34%
10%	Primary	33%

EvCol— KEY MILESTONES & EVALUATION CHECKPOINTS

Milestone	Target Date	Owner
Requirements & system design frozen	14-Aug-2026	All
Event ingestion & data foundation established	30-Aug-2026	Jaskaran/Vaani
Collision scoring logic established	12-Sep-2026	Jaskaran/Vaani
Risk scoring API integration	24-Sep-2026	Jaskaran/Parmeet
Interactive dashboard workflow	08-Oct-2026	Vaani/Parmeet
Frontend–backend–scoring integration	16-Oct-2026	All
Testing + CI/CD	31-Oct-2026	Parmeet/Vaani
Calendar sync & pilot validation	20-Nov-2026	Jaskaran/All
Final demo & submission	27-Nov-2026	All



Expected Evidence	Status	Notes
Problem statement, use cases, DFD & architecture	Complete	Foundation
External API, normalized data & Elasticsearch index	Complete	Event data pipeline
Explainable risk-scoring module	Complete	Core scoring logic
FastAPI endpoint returning risk & recommendations	In progress	Backend integration
Launch submission → risk dashboard → recommendations	Planned	First full demo
Integrated web application workflow	Planned	End-to-end integration
Automated tests + GitHub Actions	Planned	Engineering validation
OAuth calendar sync + validation results	Planned	Final validation
GitHub repo, report, working demo & presentation	Planned	Final delivery
